

Drawing Resister

Sr No	Project Name	Architecture	RCC	Plumbing	Electrical	Landscape	Over All Drawings
		% Achieved	% Achieved	% Achieved	% Achieved	% Achieved	% Achieved
1	**Youthika, Sparkle Realty**	79%	92%	81%	62%	83%	79%

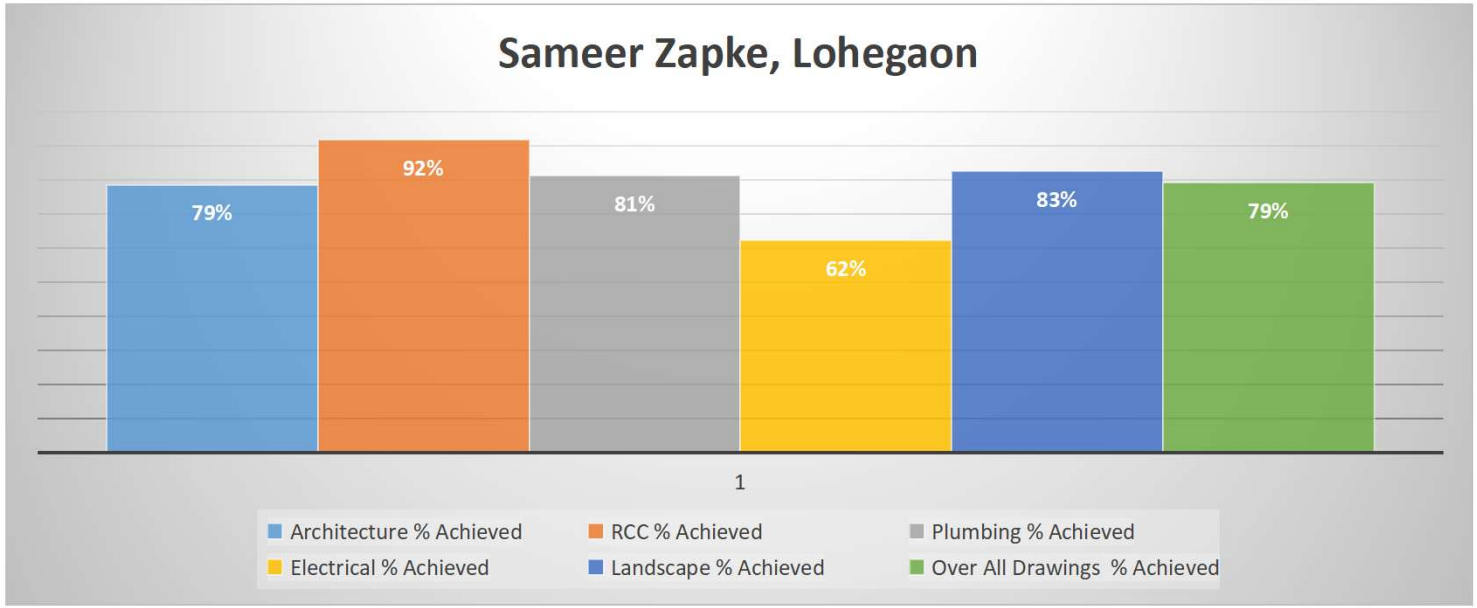

Sr No	Project Name	Building Name	Architecture	RCC	Plumbing	Electrical	Landscape
			% Achieved	% Achieved	% Achieved	% Achieved	% Achieved
1	Youthika, Sparkle Realty	A	60%	92%	87%	95%	-
		B	85%	100%	97%	92%	-
		DEVELOPMENT	91%	83%	60%	0%	83%
			79%	92%	81%	62%	83%

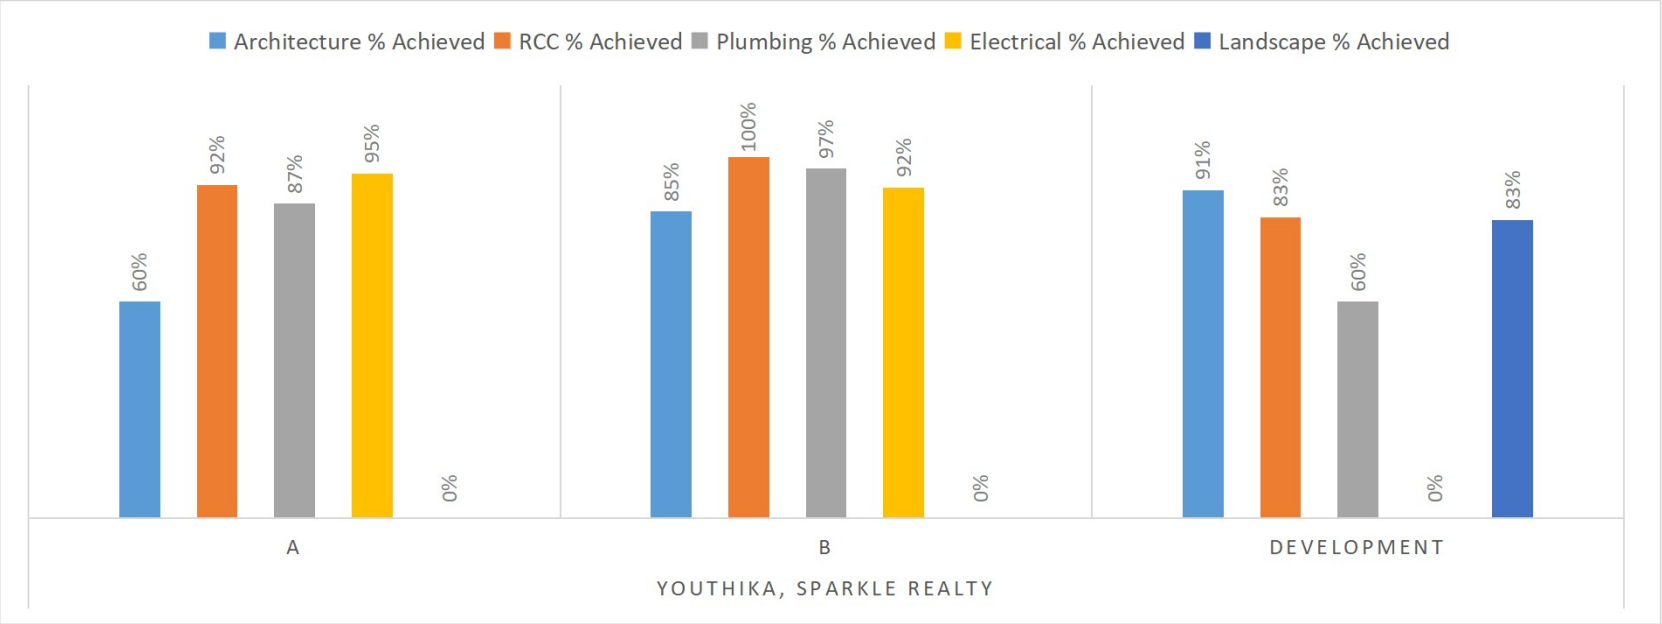

DESIGN PROGRESS REVIEW SHEET


Project Name - Sparkle Youthika

Sr. no.	Stages of coordination	Action by		Deliverables	Start Date	Duration (120 Working days)	MileStone	Status
							Target	
1	Prequalification process of consultants			**Appointment of consultants**				
2				Architect + EC - Consultant (If required)				**Appointed**
3				Landscape Architect				**Appointed**
4				MEP & Fire consultant				**Appointed**
5				Structural				**Appointed**
6	Stage 1 Master Layout, Concept design & Approval	Client/Sales team		Project Brief requirement (Project specific requirement by client)		**18**	1.0	1.0
7		Architect	Concept Design	Feasibility calculations in terms of permissible built-up, building height, ground coverage, site margins, allowable projections.			1.0	1.0
8				Conceptual master layout with block services location- UGWT,STP,Transformer, DG, OWC, Main entrance & exit gate.			1.0	1.0
9				Conceptual block sizes for STP, UGWT, Transformer OHC etc				
10				Positioning of conceptual amenity/ open space area.			1.0	1.0
11				Conceptual locations of ramp, driveways and podium location with size.			1.0	1.0
12				Conceptual typical unit layout with typical floor			1.0	1.0
13				Conceptual furniture & Toilet layout			1.0	1.0
14				Allocations of refuge areas/ floors			1.0	1.0
15				Conceptual parking layouts with traffic circulation.			1.0	1.0
16				Conceptual project's site sections			1.0	1.0
17				Discussion on Conceptual 3D views.			1.0	1.0
18							**11.0**	**11.0**
19		Client	Concept Approval	Approval on master layout with block services location- UGWT,STP,Transformer, DG, OWC, Main entrance & exit gate.			1.0	1.0
20				Approval on block sizes for STP, UGWT, Transformer OHC etc			1.0	1.0
21				Approval on Positioning of conceptual amenity/ open space area.			1.0	1.0
22				Approval locations of ramp, driveways and podium location with size.			1.0	1.0
23				Approval on typical unit layout with typical floor			1.0	1.0
24				Approval on furniture & Toilet layout			1.0	1.0
25				Approval on Allocations of refuge areas/ floors			1.0	1.0
26				Approval on parking layouts with traffic circulation.			1.0	1.0
27				Approval on project's site sections			1.0	1.0
28				Approval on Conceptual 3D views			1.0	1.0
							10.0	**10.0**
				Total			**21**	**21**
29	Stage 2 Schematic Design & Approval	Structural consultant	Column Position & Beam framing	Column positions with Tentative sizes.			1.0	1.0
30				Beam & Slab Framing layout with tentative sizes.			1.0	1
31				Conceptual shear walls/ lift cores sizes with wall thickness.			1.0	1
32							**3.0**	**3.0**
33		Architect	Unit floor plans, Master layout	Unit plans with opening schedules			1.0	1.0
34				Floor plans with lifts, staircase, fire tower.			1.0	1.0
35				Master Layout with levels as per contour			1.0	1.0
36							**3.0**	**3.0**
37		MEP consultant	MEP services Requirement	Discussion on sunk requirements for toilet, dry balcony and Attached terraces.			1.0	1.0
38				Discussion on Service slabs, its size and its levels				
39				Discussion on shaft sizes at building internal area.				
40				Confirmation of Floor to floor height at diversion levels.				
41				Tentative area for Transformer room with capacity and level			1.0	1
42				Discussion of UGWT compartment and levels				
43				Discussion of STP invert level.				
44				Discussion of Solar PV & Hot water capacities				
45							**2.0**	**2.0**
46		Architect	Parking finalsation	Finalisation of Driveaways as per tentative column Position & tentative sizes			1.0	1.0
47				Number of parkings achieved as per the column positon and tentative sizes.			1.0	1.0
48							**2.0**	**2.0**
49		Landscape Consultant	Landscape Concept & Layout	Floor plans for Club house with sections			1.0	1.0
50				Open space amenities with sections.			1.0	1.0
51				Entry and Exit Gates postion and operations.			1.0	1.0
52				Detailed landscape working drawings			1.0	1.0
53							**4.0**	**4.0**
54		Architect/Client	Finalsation of 3D views.	3D views finalisation as per the schematic design .			1.0	1
55				Approval on 3D view as per schematic design.			1.0	1
							2.0	**2.0**
				Total			**16.0**	**16.0**
56	Stage 3 Statutory Compliances		EC Compliances	Kick off meeting with Architect			1.0	1
57				Mock Meeting				
58				Submission of Relevant Data for EC file inward/Upload at Parivesh portal				
59				STATE EXPERT APPRAISAL COMMITTEE (SEAC) meeting				
60				Grant of EC				
61								
62			IOD submisson	To acquire Garden NOC			1.0	1
63				To acquire Drainage NOC				
64				To acquire Water NOC				
65				To acquire Provisional NOC				
66				Inward of IOD file				
67				Grant of IOD				
68								
69			Building Sanction	Commencement Certificate			1.0	1
				Total			**3.0**	**3.0**
70	Stage 4 Design Analysis & Detailing	Structural Consultant	RCC Structural Analysis	Structural Analysis for actual column sizes			1.0	1
71				Structural Analysis for actual beam sizes				
72				Structural Analysis for actual slab thickness				
73							**1.0**	**1.0**
74		Architect	Architectural Working Drawings	Incorporatting of Column, beam and slab size in architectural drawings			1.0	1
75				Preparation of Working drawings with framing drawings incorporated in Architecural drawings for Other Services working.				
76							**1.0**	**1.0**
77		MEP Consultant	MEP Internal Services Spaces	Position & sizes of Electrical shafts with respect to framing.			1.0	1
78				Position & sizes of Pumbing shafts with respect to framing.			1.0	1
79				Position & sizes of service ledges with respect to framing.			1.0	1
80				Positon & Sizes of pressurization shafts			1.0	1
81							**4.0**	**4.0**
82			Internal Plumbing Layout	Internal plumbing for toilets			1.0	1
83				Internal plumbing for Dry Balconies			1.0	1
84				Internal plumbing for Attached Terraces			1.0	1
85				Internal plumbing for Common area.			1.0	1
86							**4.0**	**4.0**
87			Internal Electrical Layout	Electrical Fixture & Conduit layout for Internal Unit			1.0	1
88				Electrical Fixture & Conduit layout for Common areas.			1.0	1
89				Electrical Fixture & Conduit layout for Parking floors			1.0	1
90							**3.0**	**3.0**
91			Firefighting & HVAC Layout	Fire fighting layout as per Architectural WD.			1.0	1
92				Fire fighting layout for parking floors.			1.0	1
93				Fire fighting layout for Resdential / habitual floors.			1.0	1
94				Basement ventilation system.			1.0	1
95				Common lobby ventilation system.			1.0	1
96				Toilet ventilation.			1.0	1

97							**6.0**	**6.0**
98			External Coordinated Layout	External Stormwater Layout			1.0	1
99				External HT Layout			1.0	1
100				External LT Layout				
101				Transformer Room			1.0	1
102							**3.0**	**3.0**
103		Landscape Consultant	Landscape Working Drawings	Position & Requirements for Softscape			1.0	1
104				Position & Requirements for Hardscape				
105				Specifications of landscape area.			1.0	1
106				Sections for Landscape area for RCC design.				
107				Club house concept drawings			1.0	1
108				Entrance gate details for RCC design			1.0	1
109				Compound wall for RCC design				
110				Open space amenities with sections for RCC design.			1.0	1
							5.0	**5.0**
				Total			**27.0**	**27.0**
111	**Stage 5** **Construction Drawings (Pre GFC)**	RCC consultant	RCC Pre GFC	RCC foundation			1.0	1
112				RCC Retaining wall				
113				RCC Column schedule			1.0	1
114				RCC Slab & Beam schedule				
115							**2.0**	**2.0**
116		MEP consultant	MEP Pre GFC	Internal Plumbing layout			1.0	1
117				Water Supply layout				
118				Drainage Downtake				
119				Internal Electrical Layout			1.0	1
120				Electrical SLD for internal electrical.				
121				Transformer Room Details			1.0	1
122				UGWT compartment sizes with sleeve positions				
123				STP drawings with Invert levels				
124				Solar PV layout			1.0	1
125				Solar Hot water layout routing				
126							**4.0**	**4.0**
127		Architect	Architectural Pre GFC	Parking floor level Pre GFC for consultants approval			1.0	1
128				Typical Floor Pre GFC for Consultants approval				
129				Top Terrace Floor Pre GFC or Consultants approval				
130				Amenity Floor Pre GFC (If appicable) or Consultants approval				
131				Sections for MEP Consultants approval			1.0	1
							2.0	**2.0**
				Total			**8.0**	**8.0**
132	**Stage 6** **Good For Construction Drawings**	Architect	Architectural GFC	Floor plans			1.0	1
133				Ramp details at driveway				
134				Sections				
135				Elevations				
136				Tiling layout				
137				Staircase section with Railing			1.0	1
138				Window details				
139							**2.0**	**2.0**
140		RCC consultant	RCC GFC	Foundation GFC			1.0	1
141				Retaining wall GFC				
142				Lift Raft GFC				
143				UGWT RCC drawings GFC			1.0	1
144				STP RCC drawing GFC				
145				Basement level Slab GFC (Sub structure)				
146				Ground floor level slab GFC			1.0	1
147				Typical Floor slab GFC				
148				Refuger floor slab GFC				
149				Terrace gloor slab GFC			1.0	1
150				OHWT GFC				
151				Pergola level Slab GFC (If applicable)				
152							**4.0**	**4.0**
153		MEP consultant	MEP GFC	Internal plumbing Layout GFC.			1.0	1
154				Watersupply Downtake GFC.				
155				Drainage Diversion GFC.				
156				Internal Electrical Layout GFC.			1.0	1
157				Electrical SLD GFC.				
158				Fire Fighting GFC			1.0	1
159				HVAC GFCs				
160				External Coordinated Layout GFC.			1.0	1
161							**4.0**	**4.0**
162		Landscape Consultant	Landscape Pre GFC	Club house Working drawings			1.0	1
163				External Landscape Working drawings			1.0	1
164				Setting of open space area.			1.0	1
165				Amenity area working drawings			1.0	1
							4.0	**4.0**
				Total			**14.0**	**14.0**
166	**Stage 7** **Bill of Quantites**	MEP consultant	Plumbing BOQ	Internal Plumbing BOQ			1.0	1
167				External Coordinated BOQ				
168			Electrical BOQ	Internal Electrical BOQ			1.0	1
169				External Coordinated electrical BOQ				
170			Fire Fighting BOQ	Fire fighting BOQ			1.0	1
171			HVAC	HVAC BOQ				
172		Landscape Consultant	Landscape GFC	Landscape GFC			1.0	1
							4.0	**4.0**
				Total			**4.0**	**4.0**
	Total compliance						**90.0**	**90.0**

Sparkle Youthika - DESIGN PROGRESS REVIEW SHEET

STAGES	CONSULTANT	Target in numbers	Achieved	Percentage Achieved
STAGE-1 Master Layotut, Concept design & Approval	Architect	11	11	100.0
	Client	10	10	100.0
STAGE-2 Schematic Design & Approval	Architect	7	7	100.0
	Structural consultant	3	3	100.0
	MEP consultant	2	2	100.0
	landscape consultant	4	4	100.0
STAGE-3 Statutory Compliances	EC Compliances	1	1	100.0
	IOD submisson	1	1	100.0
	Building Sanction	1	1	100.0
STAGE-4 Design Analysis & Detailing	Architect	1	1	100.0
	structural consultant	1	1	100.0
	MEP consultant	20	20	100.0
	landscape consultant	5	5	100.0
STAGE-5 Construction Drawings	Architect	2	2	100.0
	structural consultant	2	2	100.0
	MEP consultant	4	4	100.0
STAGE-6 Good For Construction Drawings	Architect	2	2	100.0
	structural consultant	4	4	100.0
	MEP consultant	4	4	100.0
	landscape consultant	4.0	4.0	100.0
STAGE-7 Bill of Quantites	MEP consultant	3	3	100.0
	landscape consultant	1.0	1.0	100.0
		90.0	90.0	100.0

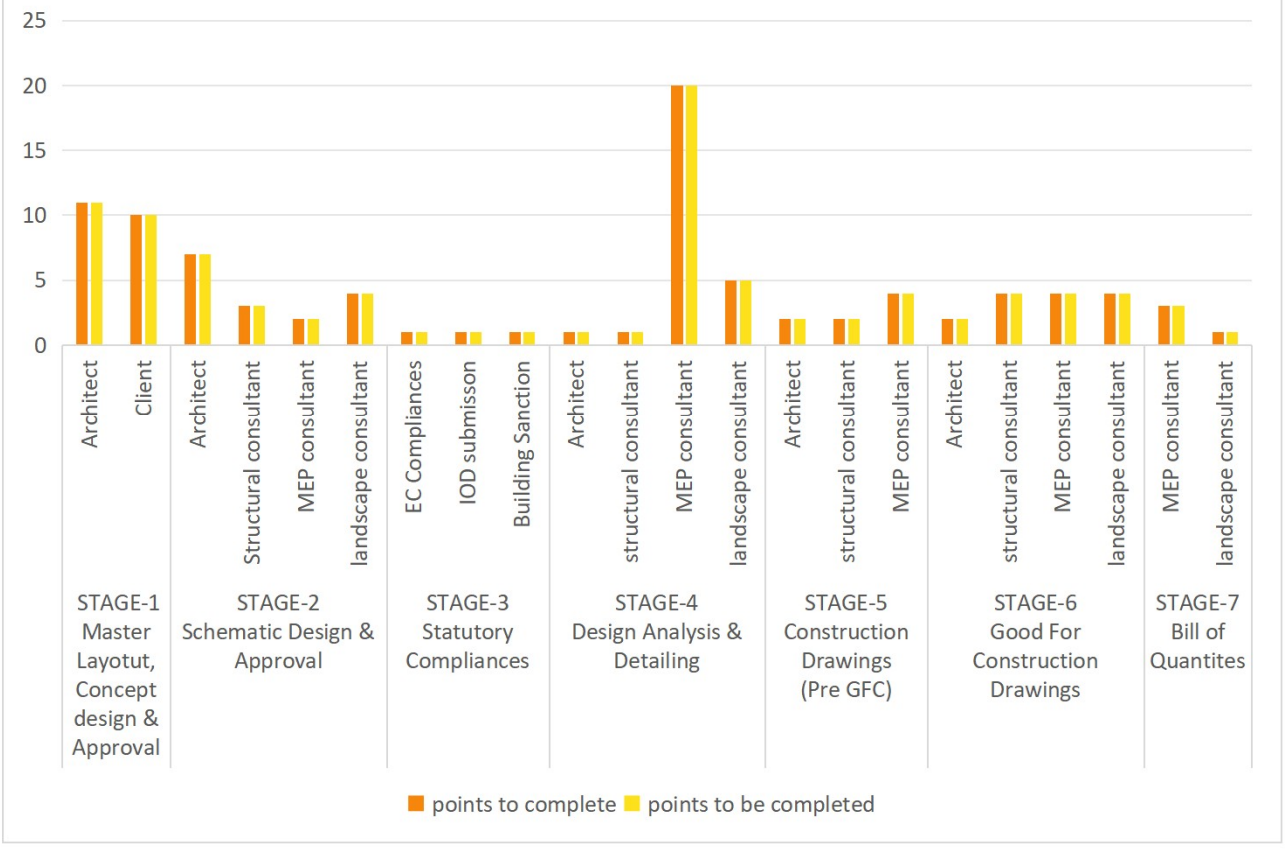

CONSTRUCTION NOTES

Youthika, Krushnarang Group, Lohegaon

				Updated on :02.07.2025
Sr. No.	Date	Descriptions of major decisions during design stage	Reference : Decision taken during Design co-ordination meeting .	Remarks
1	13.08.2022	CS For EC Uploaded.		
2	03.10.2022	We were absent in 154th seac 3 meeting due to unavailability of some documents		
3	10.10.2022	Consultant Kickoff meeting done.	MOM1	
4	10.10.2022	EC Process for the project extended by 15 days.	MOM1	
5	19.10.2022	Parking to be updated.	MOM1	
6	21.10.2022	Parking layout to be taken as clear open space, No podium	Telephonic discussuion with Samir sir, Dixit Sir	
7	29.11.2022	159th agenda was published to which we haven't been selected form their side. (Depends on them as random selection pattern)		
8	21.03.2023	1.Internal planning affected due to flat sale issue (Common bathroom Ventilator Issue). 2.Informed to Architect on whatsapp at 17.03.2023, Architect Informed in consultant group on 21.03.2023. 3.Approval given By Client on 23.03.2023, updated drawing expected at same date. **Note - RCC column positioning & Beam Framing will get updated**	Telephonic & Whatsapp disscussion with Ar Atul Sir, Mr Samir Sir	
9	13.07.2023	L.V room removed from planning as suggessted by architect and client	Telephonic discussion with architect and mail approval from client	value engineering done of 98,000
10	01.08.2023	Project Shuffle, Transition Saurabh to Arzoo	HO Meeting	
11	21.08.2023	depth of beam finalised as 700, with approval of the client.	Telephonic discussion and over project whats app group	
12	31.08.2023	Architectural WD for B building delayed due to architects leave.	drawings are delayed.	
13	01.09.2023	First slab peripherry sunk in driveway confirmed as -	point raised by RCC consultant approved from mep and arch over whats app group	
14	04.11.2023	Quaterly consultant meeting on site with all.		
15	25.11.2023	stilt height is less by 100mm , beam depth revised to 600		
16	17.05.2024	Project Shuffle, Transition Arzoo to Saurabh	HO Meeting	
17	25.05.2024	Site Visit + Audit done		
18	15.06.2024	B-wing- As per height requirement,OHWT location changed.	Location marked by MEP consultant approved from RCC and arch over mail.	
19	12.08.2024	Landscape design changes by sumit sir. (half area utilized for OHWT and solar area and half area utilized for lanscape working)	Telephonic & Whatsapp disscussion with poonam mam.	
20	24.09.2024	Compound wall design revised	Design changes by client.mail from poonam mam.	
21	15.10.2024	changes regarding Entrance gate	Design changes by client.mail from poonam mam.	
22	13.11.2024	Entrance gate drawing revised.	As per Telephonic discussion with poonam mam. Design Comments Recieved from client.	
23	26.12.2024	The client has approved the release of the R0 GFC drawing for the B-Wing top terrace. Howe	As per telephonic discussion with poonam mam. and via.on the mail also.	
24	30.01.2025	the width of the pergola needs to be reduced. The reason for this change is that the terrace space is not being utilized effectively due to the pergola on the terrace floor in 'Wing A'.	As per the telephonic discussion with Poonam Ma'am , the same discussion was held with the client	
25	25.02.2025	The column of the entrance gate is obstructing the transformer room, requiring a revision of the transformer room layout.	Design changes by client.mail from poonam mam.	
26	07.04.2025	Revised club house for sanction drawing updation	Mail from Architect	
27	26.06.2025	All shrub areas and seating arrangements located under the pergola on the terrace are to be removed. Reason: Due to the limited height of the pergola, the space is not functionally usable.	Design changes by client.mail from poonam mam.	
